

Minnehaha Elementary School

ICS Weekly Progress Report Friday – March 29th, 2024

Address: 421 7th Street Two Harbors, MN 55616

Minnehaha Elementary School

Completed week March 29th, 2024

- Continued painting touch-ups
- Completed bathroom accessory installation
- Continued demo of kitchen/cafetoria area
- Began underground plumbing
- Continued punch list items

Upcoming Work

- Complete demolition of kitchen/cafeteria
- Continue underground plumbing
- Begin electrical rough-ins
- Begin steel stud framing



Minnehaha Elementary School

ICS Weekly Progress Report Friday – March 29th, 2024

Address: 421 7th Street Two Harbors, MN 55616

Progress Photos




Kitchen completed. Staff moved-in and starting using new space



Minnehaha Elementary School

ICS Weekly Progress Report Friday – March 29th, 2024

Address: 421 7th Street Two Harbors, MN 55616

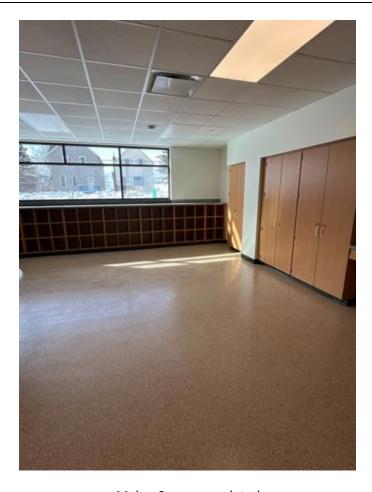


Maker Space completed



Minnehaha Elementary School

ICS Weekly Progress Report Friday – March 29th, 2024

Address: 421 7th Street Two Harbors, MN 55616

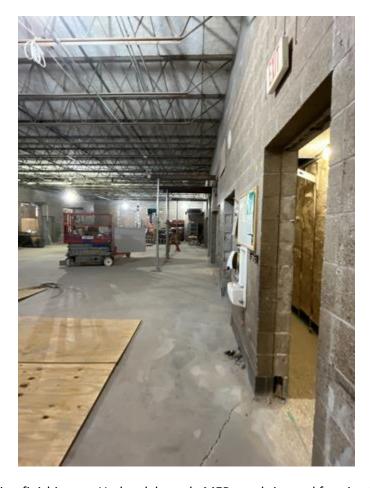

Demolition finishing up. Under slab work, MEP rough-ins and framing to follow
