

Lake Superior Schools

William Kelley Addition and Renovation

ICS Weekly Progress Report Friday – July 28, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614

William Kelley Addition and Renovation

🕸 Completed week ending July 28, 2023

Continued electrical, and mechanical rough in.
Finished pouring of concrete for main entrance addition.
Continued painting walls, soffits, and wall patches.
Continued patching of ceiling grid.
Continued drywall, tape, and mudding.
Started VCT floor installation in classrooms.
Started setting door frames.
Forming exterior stair steps
Started setting bathroom fixtures.

👻 Upcoming planned work

Backfill soils for main entrance addition.
Form piers and other structures for main entrance addition
Continue electrical, and mechanical rough ins.
Continue painting wall patches.
Continue patching of ceiling grid.

Continue drywall, tape, and mudding.

Finish setting bathroom fixtures.

Forms footings and foundations for music suite addition

Pour exterior stair steps.



ICS Weekly Progress Report Friday – July 28, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614

Progress Photos



Footings and foundations poured for main entrance addition.



New stairwell walls poured.



ICS Weekly Progress Report Friday – July 28, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614



Soffits and wall framing for flex nooks and display case outside science classrooms.



Classroom painting and floor installation



ICS Weekly Progress Report Friday – July 28, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614



Painting soffits in new flex space




Painting walls in new flex space



ICS Weekly Progress Report Friday – July 28, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614

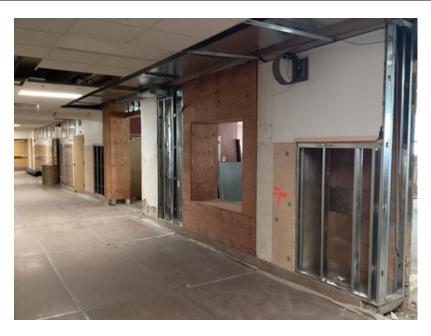

Outside of Media Center Wall and Display Case Framing



Science Classrooms plumbing and electrical rough ins.
