



William Kelley Addition and Renovation

ICS Weekly Progress Report Friday – August 25, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614

William Kelley Addition and Renovation

Completed week ending August 18, 2023

- Tape-Mud- Walls in Science Rooms
- Taping and mudding of walls in kitchenette and conference room
- Installed steel decking for the main entrance.
- **Exterior** wall framing at main entrance.
- Poured last foundation north wall for music suite
- Polish terrazzo flooring.
- Punch list work for classrooms
- Waxing and cleaning classrooms
- Toilet partitions installed.
- Seed blankets for grass at new concrete stairs
- Installed door hardware.
- Furniture moved into classrooms.
- Staff move in.

Upcoming planned work

- Punch list
- Finish demolition/removal of existing boiler
- Seal terrazzo flooring
- Finish interior glass and wall tile installation.
- Testing and balancing of mechanical systems
- Finish installing toilet accessories
- Finish door hardware
- Science Rooms paint
- Science Rooms ceiling grid
- Painting of walls in kitchenette and conference room
- Temporary handrails at exterior stairs
- Continue exterior wall framing at main entrance.





William Kelley Addition and Renovation

ICS Weekly Progress Report Friday – August 25, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614

Progress Photos



Exterior wall framing at new main entrance



Music Addition north wall foundation poured






William Kelley Addition and Renovation

ICS Weekly Progress Report Friday – August 25, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614



Classroom move in

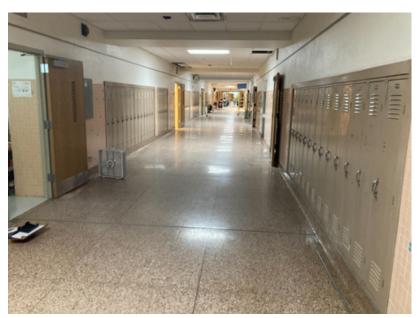

Corridors cleared and cleaned






William Kelley Addition and Renovation

ICS Weekly Progress Report Friday – August 25, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614

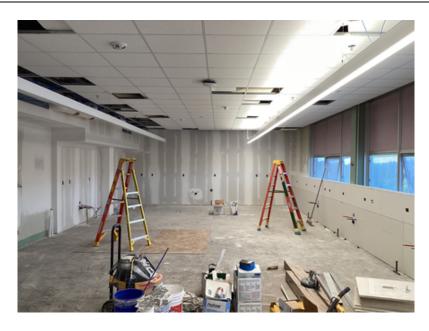

Science Room Drywall Tape and Mud







William Kelley Addition and Renovation

ICS Weekly Progress Report Friday – August 25, 2023

Address: 137 Banks Blvd. Silver Bay, Minnesota 55614



Toilet partition installation
